


WORK ORDER (WELDED)

Customer:	yogita	Job No:	ORD-1782736471409
Reference:		Print Date:	29/06/2026
System:	Sunny Plast 70mm	Design:	1 line(s)
Width × Height:	0 × 0 mm	Quote#:	ORD-1782736471409

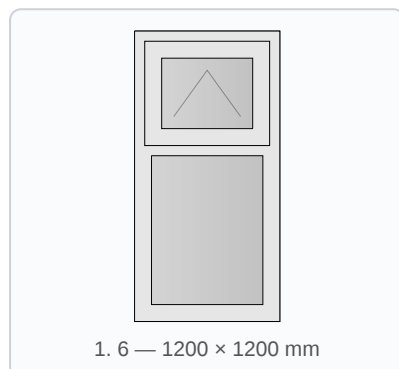

Welded cut list. Lengths below INCLUDE the welding-shrinkage allowance — cut bars to these sizes. After welding, the finished assembly returns to the ordered dimensions.

Sections Required							
H/V	Section	Description	Qty	Length	End Prep	Reinforcing	Reinf Length
Hor	Frame	Frame 5 Chamber	2	1206	\ - /		
Vert	Frame	Frame 5 Chamber	2	483	\ - Y]		
Vert	Frame	Frame 5 Chamber	2	723	[Y - /		
Hor	Frame	Chasement Z Sash	1	1206	< - >	REINF-13x29	1072
Hor	Sash	T Sash	2	1134	\ - /	REINF-28x24	970
Vert	Sash	T Sash	2	444.5	\ - /	REINF-28x24	280.5
Hor	Bead	28mm Bead	2	1010	[-]		
Vert	Bead	28mm Bead	2	320.5	[-]		
Hor	Bead	28mm Bead	2	1112	[-]		
Vert	Bead	28mm Bead	2	662.5	[-]		
Hor	Sash	13 x 29 Steel Reinforcement	1	1072	[-]		
Hor	Sash	28 x 24 Steel Reinforcement	2	970	[-]		
Vert	Sash	28 x 24 Steel Reinforcement	2	280.5	[-]		

Accessories Required		
Description	Qty	Unit Of Measurement
White Inline Handle	1	Unit
1000mm Espagnolette	1	Unit
10" Friction Hinge	1	Unit
Mushroom Striker	4	Unit
Run Up Block	2	Unit
Glazing Bridge Packer	13	Unit
Gasket 01	6266	Metres

Description	Qty	Unit Of Measurement
Gasket 02	6158	Metres

Glass Required			
Description	Qty	Width	Length
01 (Frame-root.top) 4-20-4 Clear Low E : Thermal Spacer Bar	1	1007	317.5
02 (Frame-root.bottom) 4-20-4 Clear Low E : Thermal Spacer Bar	1	1102	652.5
